



# PREPARATIONS FOR TUVALU'S FIRST BIENNIAL TRANSPARENCY REPORT

Presenter: Joanna Latasi

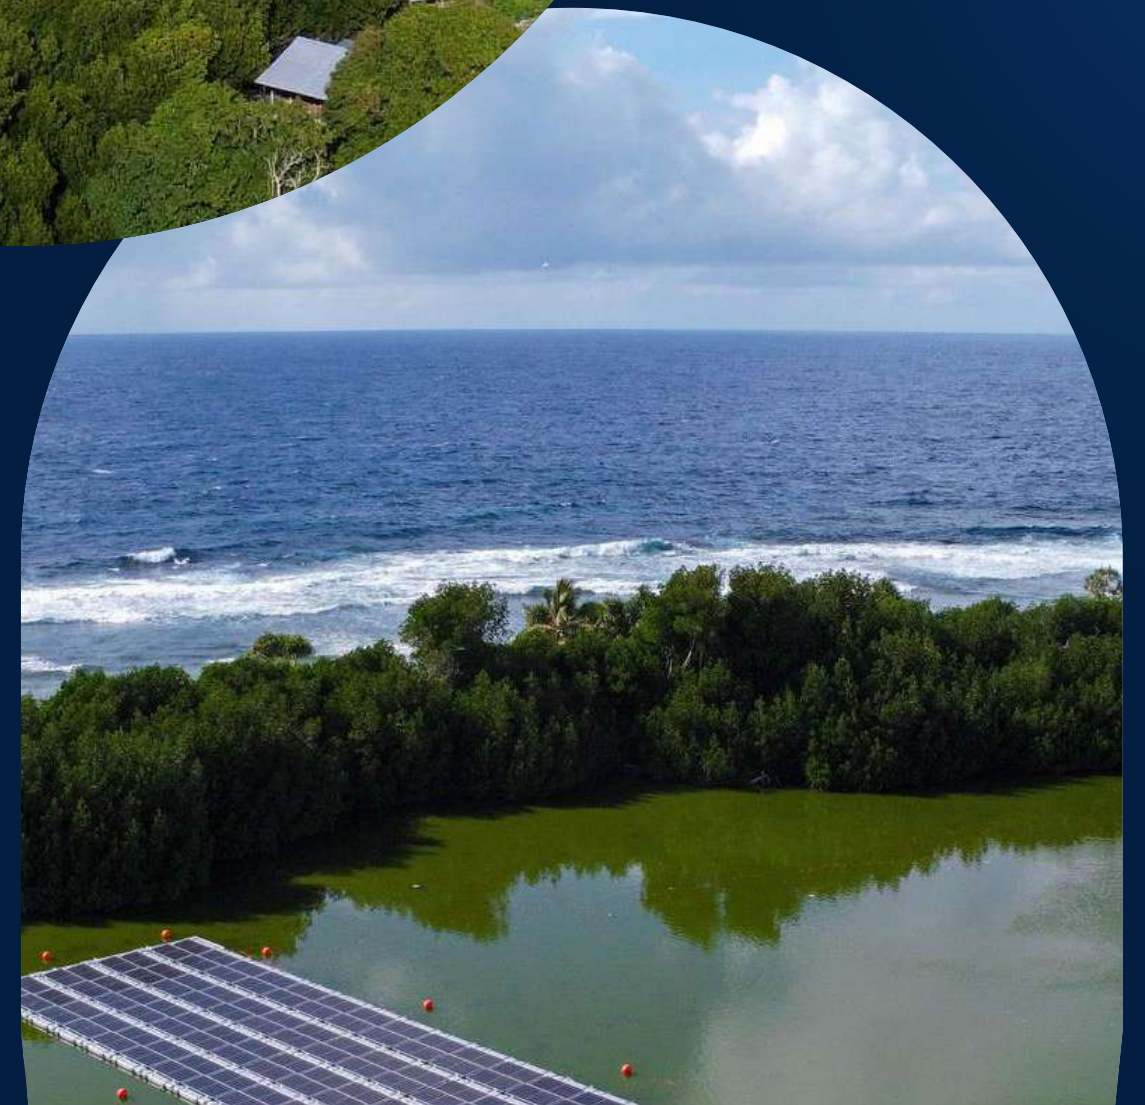

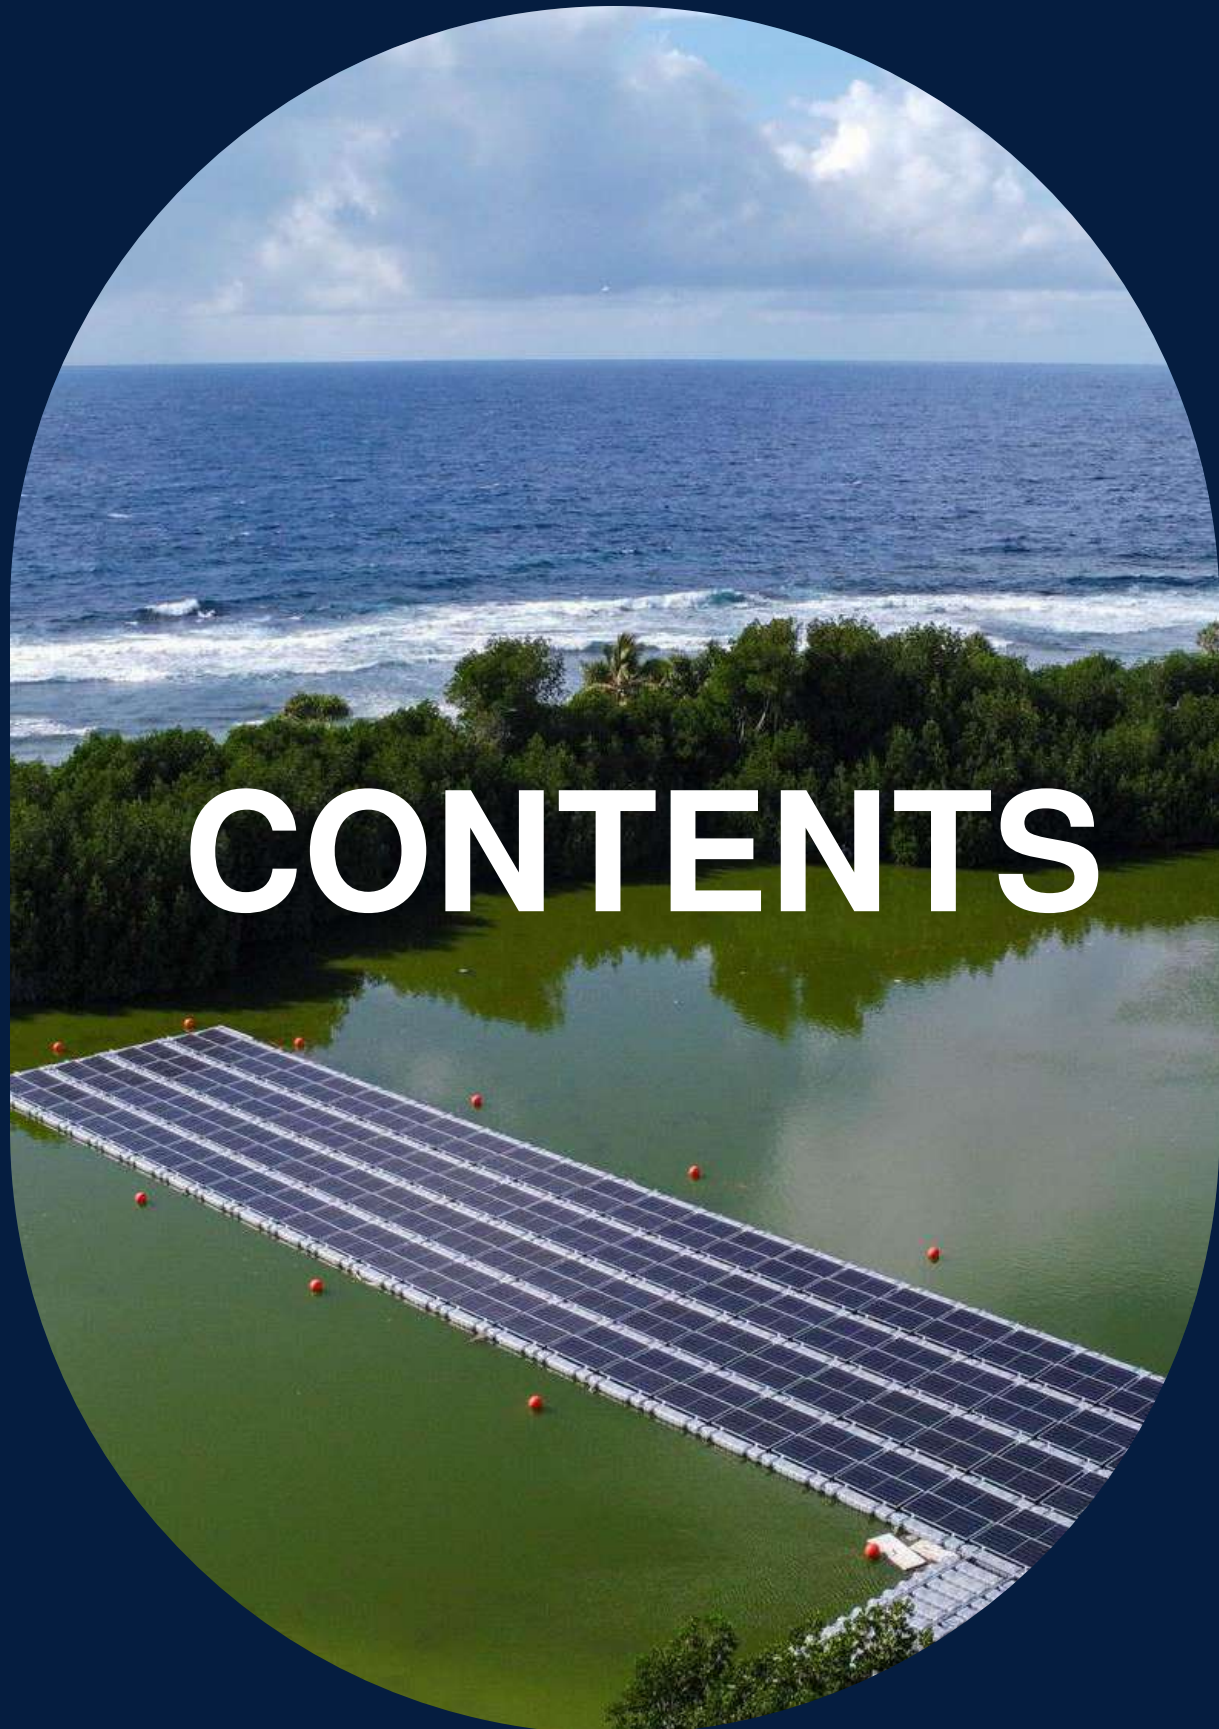

# CONTENTS

01

About the project

02

What to expect

03

Key events

04

Challenges

05

Outcomes

06

Key takeaways

07

Lessons Learned

08

Good Practices

09

Way Forward

# 01 ABOUT THE PROJECT



## DONOR

Global Environment Facility



## IMPLEMENTING PARTNER

United Nations  
Environment Programme



## EXECUTING AGENCY

Tuvalu Climate Change  
Department under the MHACCE



## BUDGET

US\$250,000 - A top up to  
the TNC budget



## TIMELINE

Technical & Implementation  
phase is from 2024 - 2026



## PROGRESS

Completed Final Draft

# 02

## WHAT TO EXPECT

When preparing your country's BTR, these are some of the factors to consider:

### Shift in Project Timeline

- Always consider a change in the project timeline.

### Project activities delay

- This might result from technical issues. Late signing of project agreement.

### Limited financial budget

- This can cause difficulties in the project delivery.

### Data gaps

- There are gaps, missing and no updated data.

### Communication breakdown

- There can be misunderstandings & miscommunication between the project & stakeholders

### Stakeholder engagement

- Expect a lack of stakeholders' engagement and data provision.

### Change in Government

- This can change government priorities & processes

# 03

# KEY EVENTS



BTR Preparation – Project implementation plan, budget and alignment to government processes



BTR Fund Approval - Project Cooperation Agreement signed, project implementation begins.



Engagement of international consultant - direct contract.



Review the draft BTR document - Stakeholders and UNEP CCC



Validation workshop - to validate the draft BTR document



Final Draft BTR Document completed



## 04 CHALLENGES

Project Planning

Information & Data Collection

Use of ETF tools

Stakeholder Coordination & engagement

Timeline & Budget

Government Processes

Staff turnover

Lack of in-country technical experts.



05

# OUTCOMES & KEY ACHIEVEMENTS



**SIGNED PCA**



**TORS & CONTRACTS DEVELOPED**



**PMU RECRUITMENT &  
ENGAGEMENT OF CONSULTANT**



**VALIDATION WORKSHOP**



**FINAL DRAFT OF BTR**

06

## KEY TAKEAWAYS

- Consultancy work
- Stakeholders' review of the BTR 1st Draft
- Technical Support
- Capacity building & training programs



07

# LESSONS LEARNED



**SUPPORT**



**COLLABORATION**



**TOOLS**



**DELAYS**



**PROGRAMS**



08

# GOOD PRACTICES

## PARTNERSHIP

---

STRENGTHEN OUR PARTNERSHIPS AND COLLABORATE MORE THROUGH REGIONAL WORKSHOPS.

## AWARENESS

---

VALIDATION WORKSHOP WITH STAKEHOLDERS AND SOCIAL MEDIA UPDATES

## COMMUNICATION

---

HAVING ACTIVE & CLEAR COMMUNICATION WITH OUR STAKEHOLDERS



09

# WAY FORWARD



\* Finalize, publish & submit to UNFCCC

\* Draft Proposal – Bundled project Btr2/Btr3 & NC4

# OUR TEAM



**JOANNA  
LATASI**

**COORDINATOR**



**MILA  
SIALE**

**ASSISTANT &  
FINANCE OFFICER**

# THANK YOU

CONNECT WITH US.

 +688 7112797

 [latasijoanna@gmail.com](mailto:latasijoanna@gmail.com)

